


## SH 45 STUDIES COMPLETED TO DATE

- Geologic Assessment
  - Karst Surveys of 100% of the SH 45 Right-of-Way
  - Soil Infiltration Studies
  - Bear Creek Recharge Study
  - Archaeological Surveys
  - Drafted *Overview and History* Section of EA
  - Drafted *Effectuated Environment* Section of EA
  - *Indirect and Cumulative Analysis* in progress
- 
-

45 SW Environmental Assessment

CSJ 0114-02-053

(State Approval) Schedule  
26 Months

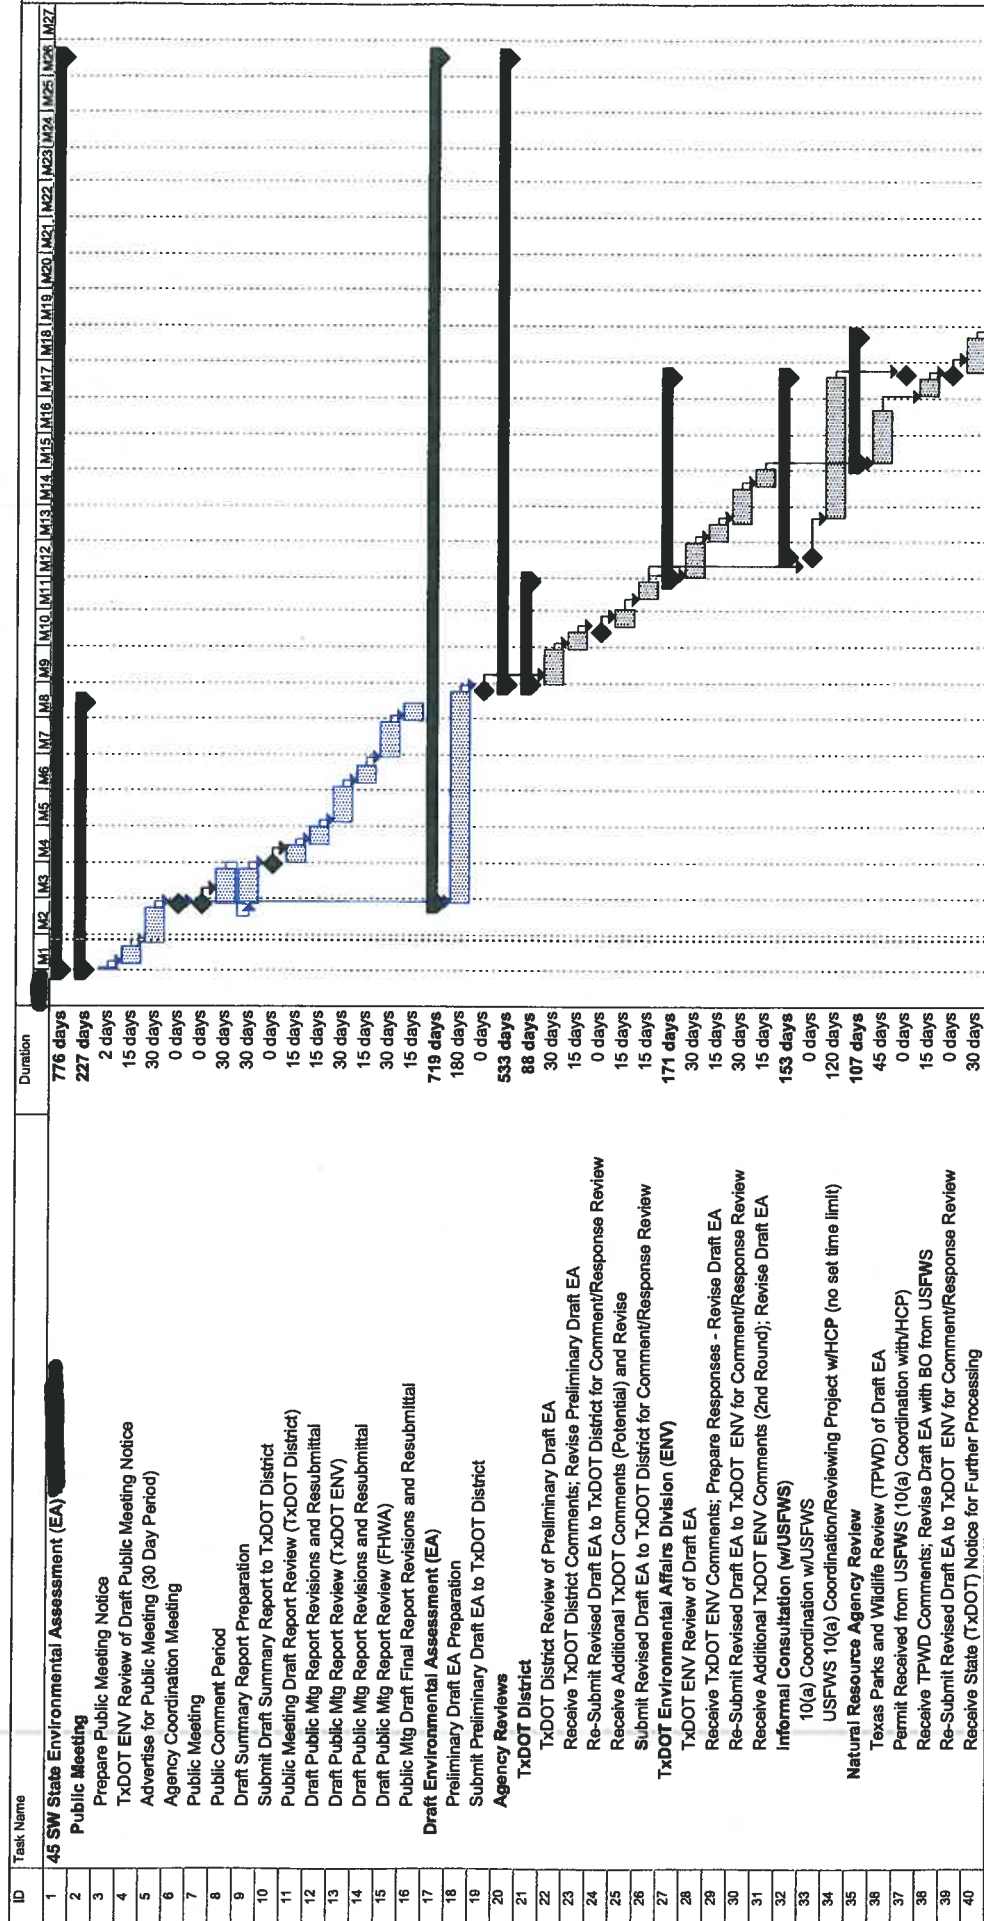

Legend:

- Task: Solid black bar
- Progress: Dotted black bar
- Milestone: Diamond symbol
- Summary: Stippled bar
- Roll Up Task: Dotted bar with arrow
- Roll Up Milestone: Diamond with arrow
- Roll Up Progress: Solid black bar with arrow
- Split: Dotted bar with vertical line
- External Task: Stippled bar with arrow
- Deadline: Arrow pointing to a date
- Project Summary: Thick solid black bar
- Group By Summary: Thick dotted black bar


CSJ 0114-02-053  
Date: Sun 4/20/09

45 SW Environmental Assessment

CSJ 0114-02-053

(State Approval) Schedule  
26 Months

ID	Task Name	Duration	LM1	LM2	LM3	LM4	LM5	LM6	LM7	LM8	LM9	LM10	LM11	LM12	LM13	LM14	LM15	LM16	LM17	LM18	LM19	LM20	LM21	LM22	LM23	LM24	LM25	LM26	LM27	
41	Public Hearing / Summary and Analysis Review	191 days																												
42	Planning and Coordination Meeting with Agency	0 days																												
43	TxDOT District and ENV Review of Draft Public Hearing Notice	15 days																												
44	Advertise for Public Hearing	30 days																												
45	Public Hearing (PH)	0 days																												
46	Public Comment Period	0 days																												
47	Preliminary Draft Summary and Analysis Report (SAR) Preparation	30 days																												
48	Submit Preliminary Draft PH_SAR to TxDOT District	0 days																												
49	TxDOT District Review and Comments	15 days																												
50	Receive TxDOT District Comments; Revise Preliminary Draft PH_SAR	15 days																												
51	Submit Revised Draft PH_SAR to TxDOT ENV	0 days																												
52	TxDOT ENV Review and Comments	30 days																												
53	Receive TxDOT ENV Comments; Revise Draft PH_SAR	15 days																												
54	Submit Revised Draft EA and Revised PH_SAR to TxDOT District and ENV	0 days																												
55	Decision	34 days																												
56	State (TxDOT ENV and District) Review Draft Final EA/SAR	30 days																												
57	Receive Approval/Environmental Clearance	0 days																												

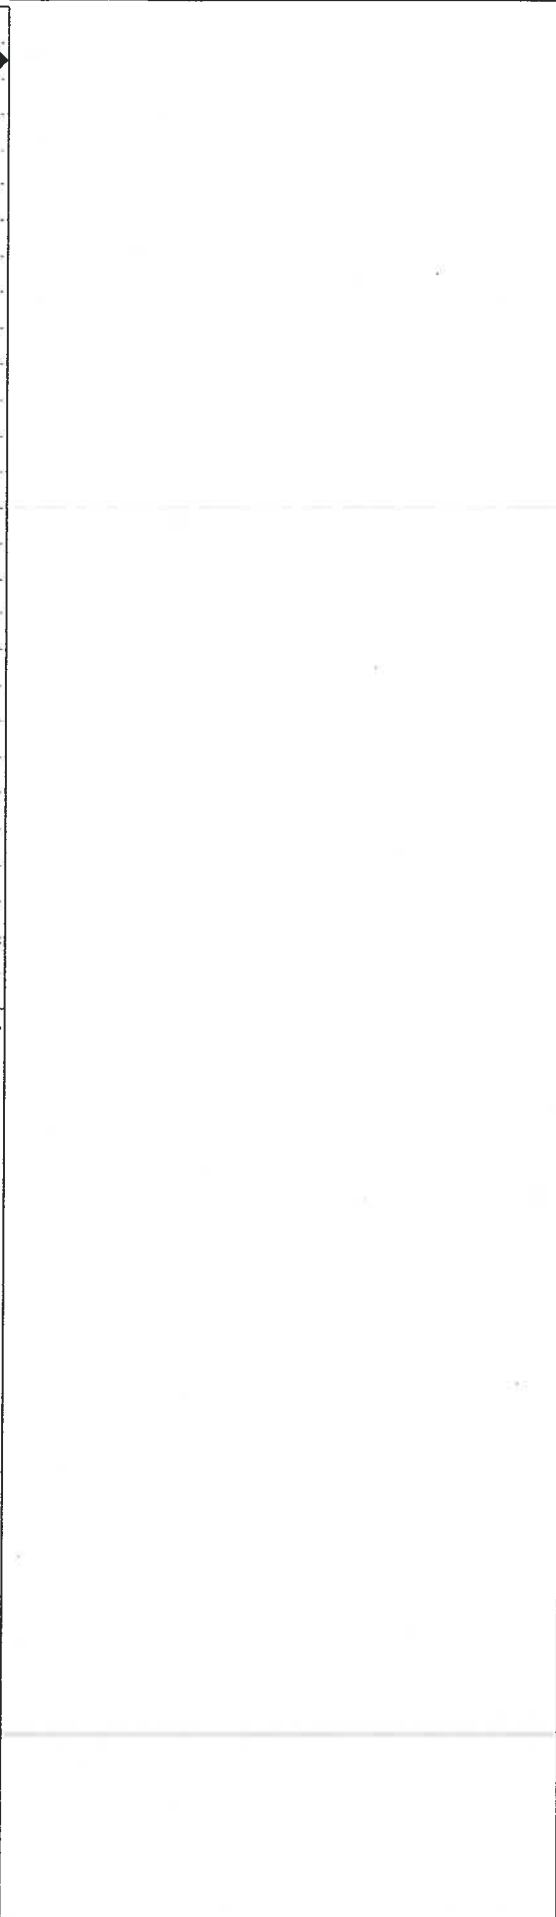


Task: Summary: Rolled Up Progress: Project Summary:   
 Progress: Rolled Up Task: Split: Group By Summary:   
 Milestone: Rolled Up Milestone: External Tasks: Deadline:

45 SW Environmental Impact Statement

CSJ 0114-02-053

(State Approval) Schedule  
40 Months

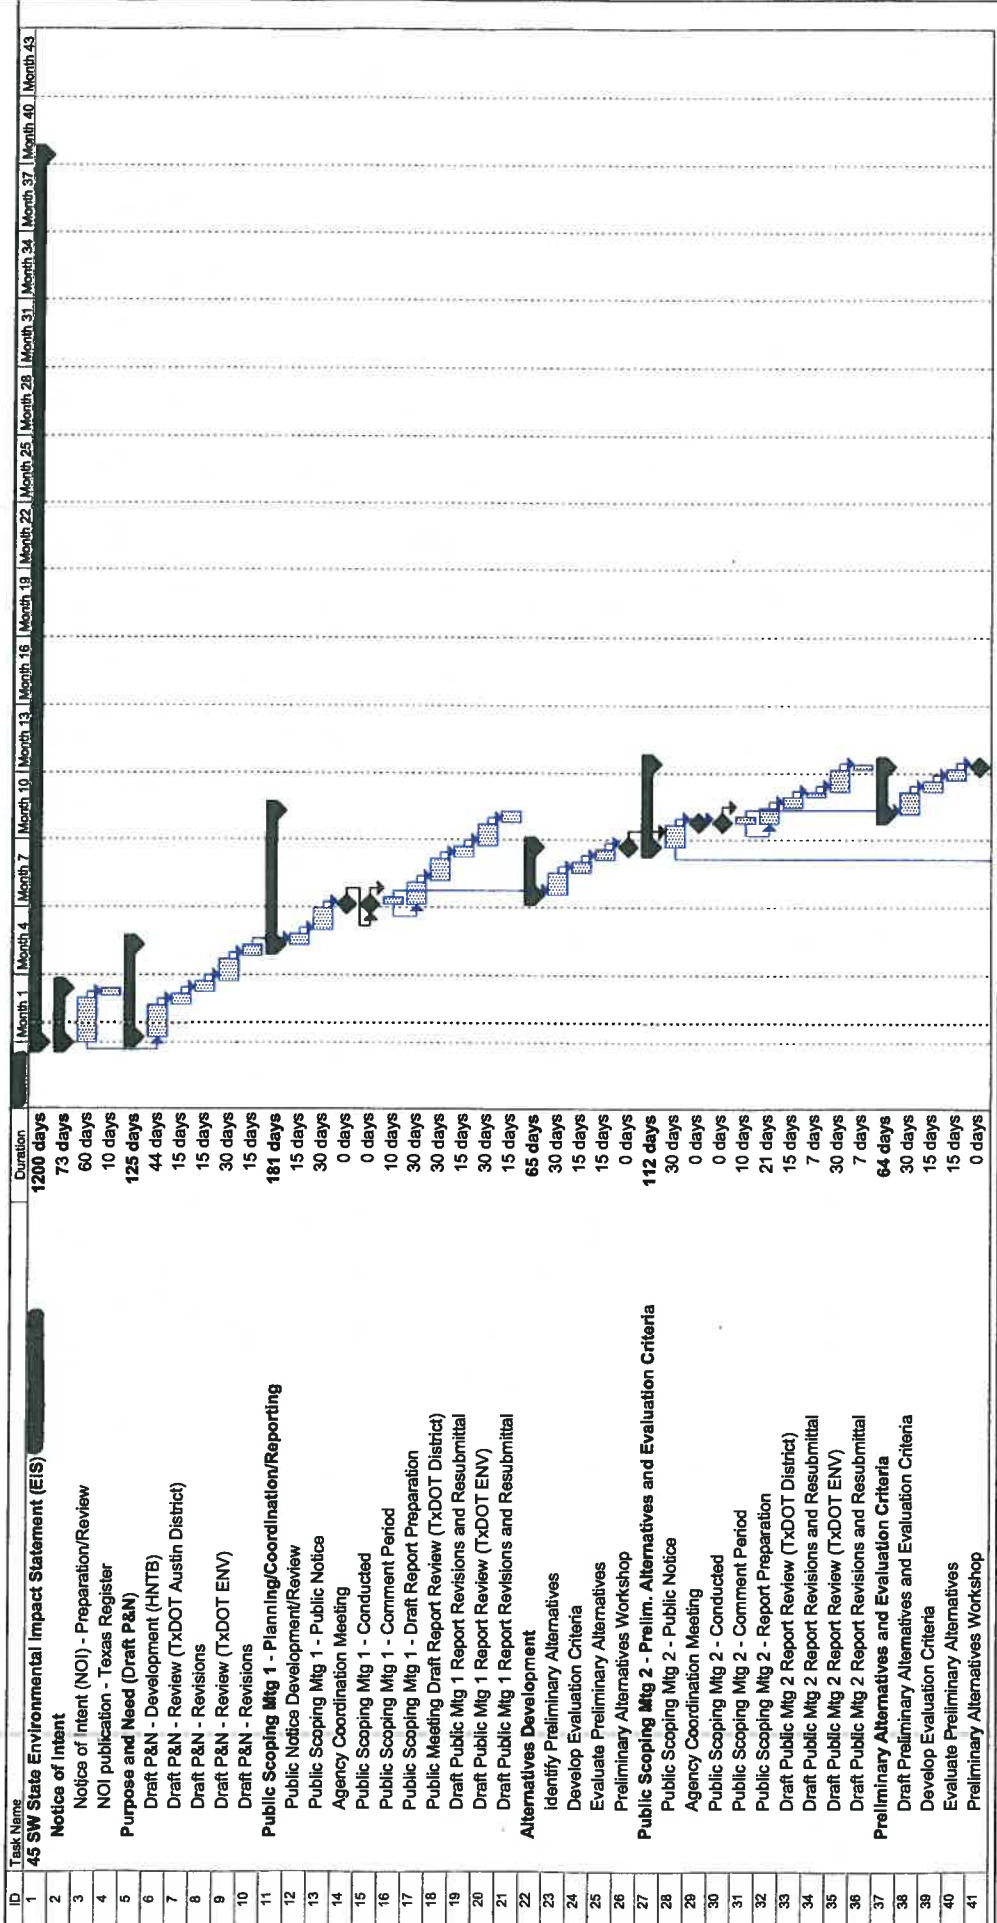


HNTB 395887TechProd\WVA\Schedule  
 45SW StateEIS\_Schedule\_042609v3  
 CSJ 0114-02-053  
 Date: Sun 4/26/09

Legend:  
 Task: [Solid Bar]  
 Progress: [Hatched Bar]  
 Milestone: [Diamond]  
 Summary: [Dotted Bar]  
 Rolled Up Task: [Dotted Bar with Arrow]  
 Milestone: [Diamond]  
 External Tasks: [Dotted Bar with Arrow]  
 Split: [Arrow]  
 Project Summary: [Thick Solid Bar]  
 Group By Summary: [Thick Solid Bar]  
 Deadline: [Arrow]

45 SW Environmental Impact Statement

CSJ 0114-02-053

(State Approval) Schedule  
40 Months

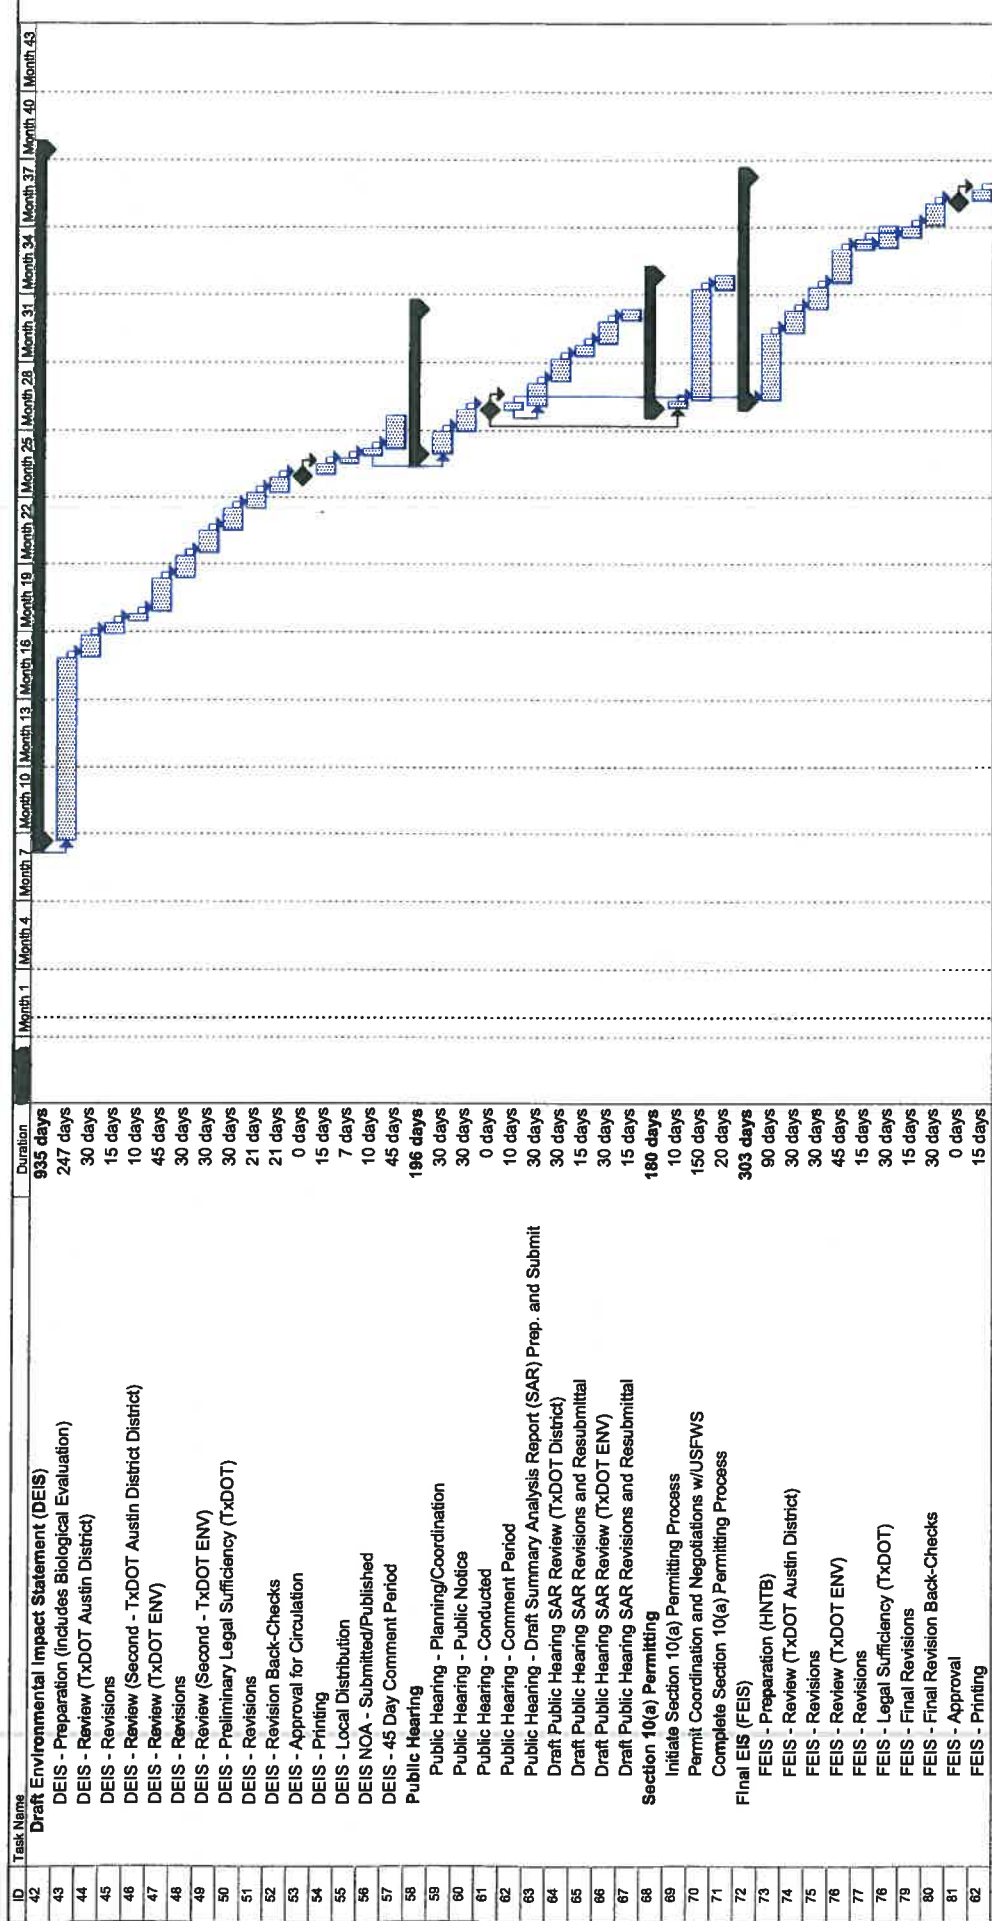


Summary  
 Task  
 Progress  
 Milestone  
 Rolled Up Progress  
 Rolled Up Task  
 Rolled Up Milestone  
 Group By Summary  
 Split  
 External Tasks  
 Deadline

45 SW Environmental Impact Statement

CSJ 0114-02-053

(State Approval) Schedule  
40 Months


ID	Task Name	Duration	Month -3	Month -1	Month 1	Month 4	Month 7	Month 10	Month 13	Month 16	Month 19	Month 22	Month 25	Month 28	Month 31	Month 34	Month 37	Month 40	Month 43
83	FEIS - Local Distribution	7 days																	
84	State Notice - Submitted/Published	10 days																	
85	30 Day Comment Period	30 days																	
86	Record of Decision - Preparation/Review/Approval	70 days																	
87	Target Date - State Decision	0 days																	




HNTB 385681 TechProc\WA\4\Schedule 45SW StateEIS_Scenario4_042009ver3	CSJ 0114-02-053 Date: Sun 4/26/09
--	--------------------------------------

45 SW Environmental Assessment

(Federal Approval) Schedule  
41 Months

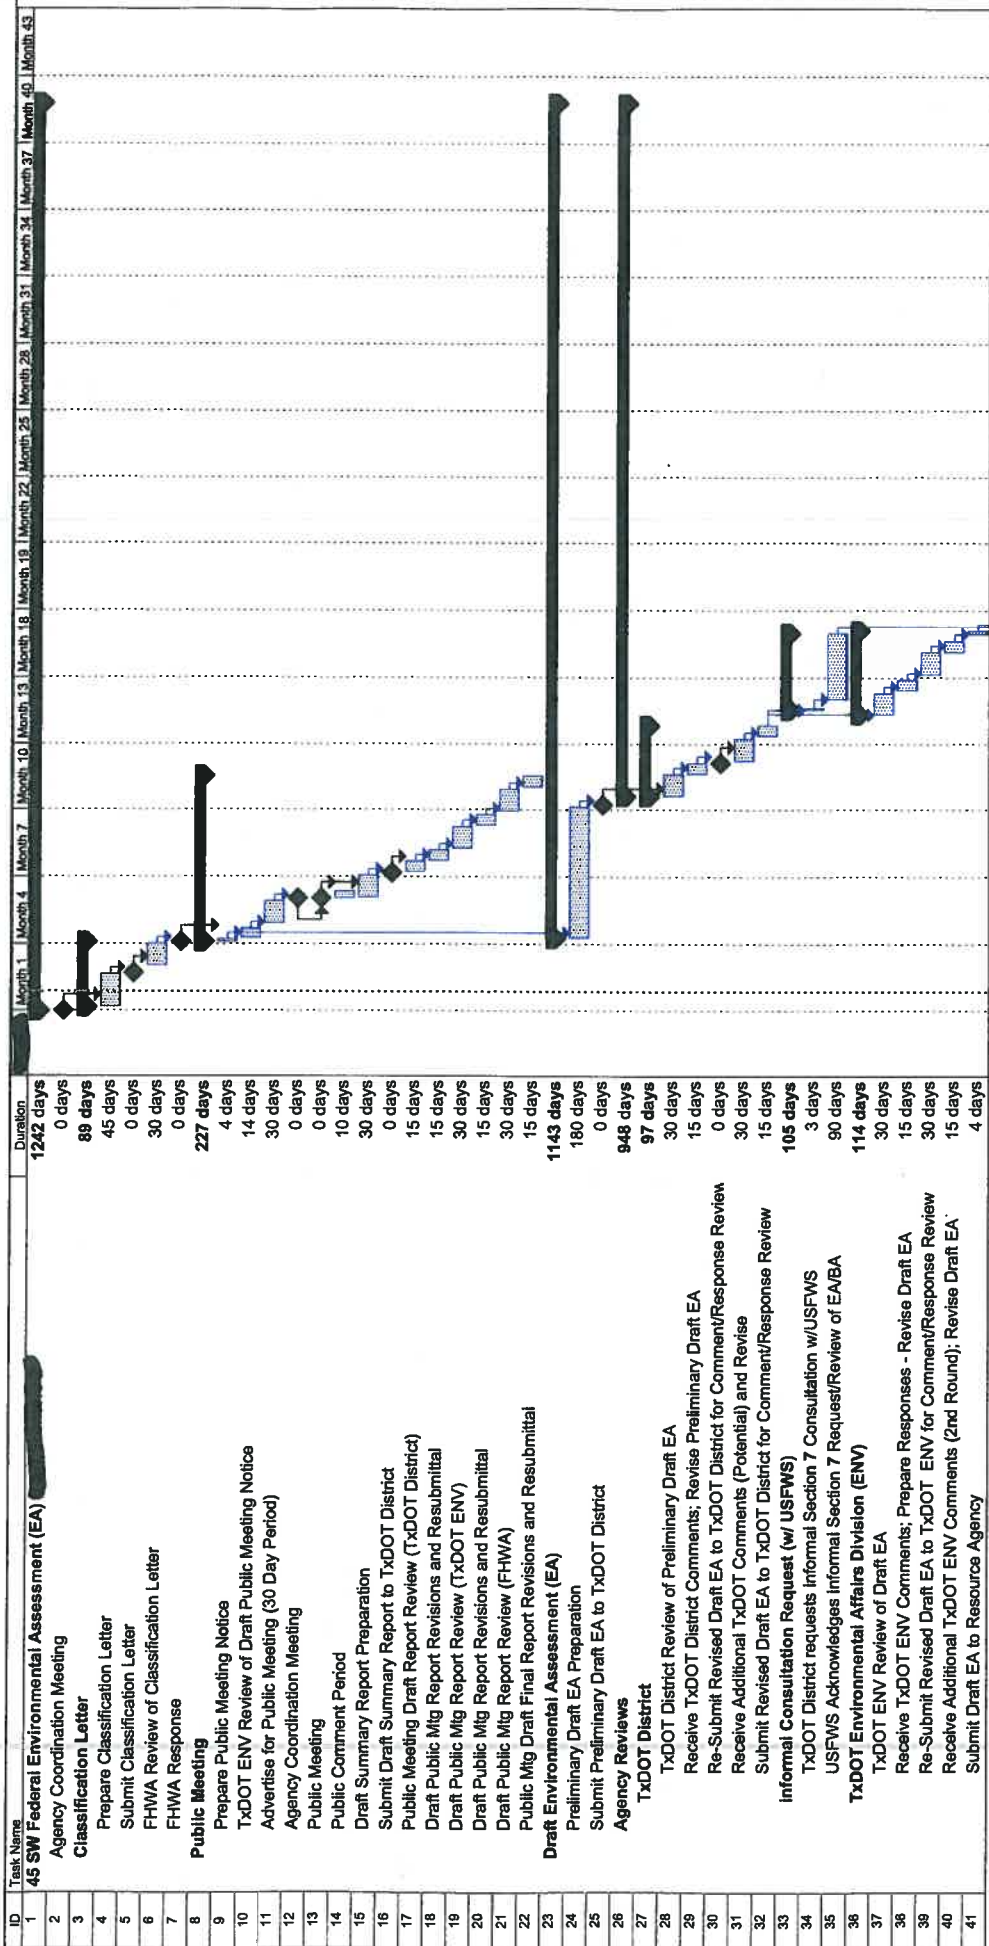

Summary  
 Task  
 Progress  
 Milestone  
 Rolled Up Progress  
 Rolled Up Task  
 Rolled Up Milestone  
 Split  
 External Tasks  
 Project Summary  
 Group By Summary  
 Deadline

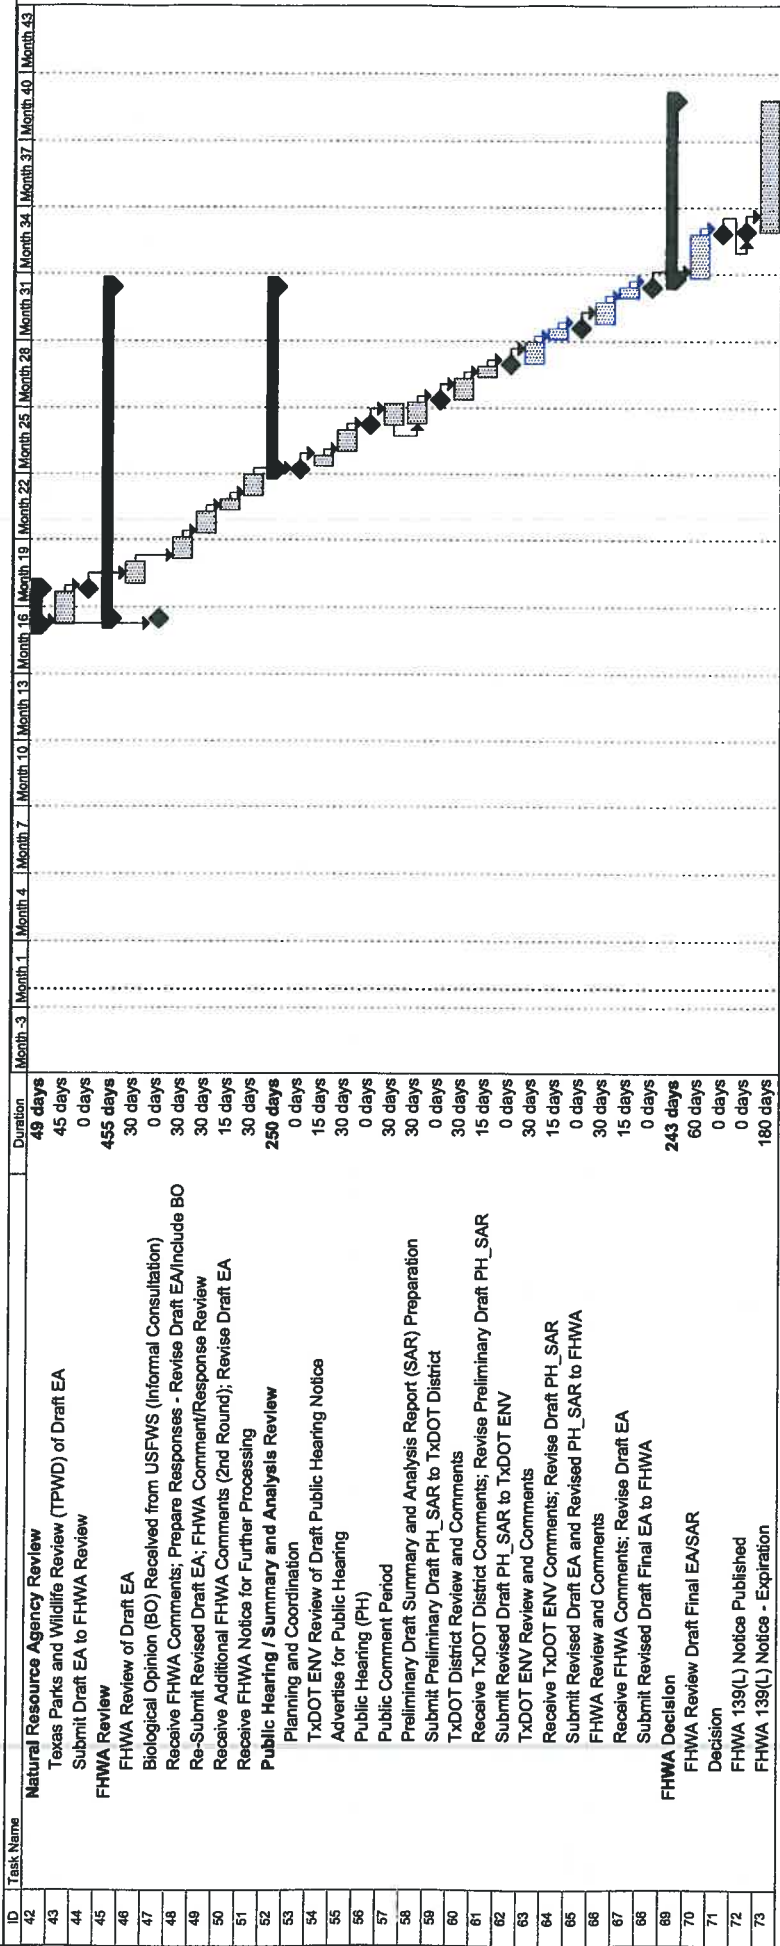

HNTB 99585TschProf/WA14Schedule  
45SWFederalEA\_Scenario2\_042508ver7

CSJ 0114-02-053  
Date: Sun 4/26/09

Task  
Progress  
Milestone


Summary  
Rolloled Up Task  
Rolloled Up Milestone

Rolloled Up Progress  
Split  
External Tasks

Project Summary  
Group By Summary  
Deadline

(Federal Approval) Schedule  
51 Months

CSJ 0114-02-053

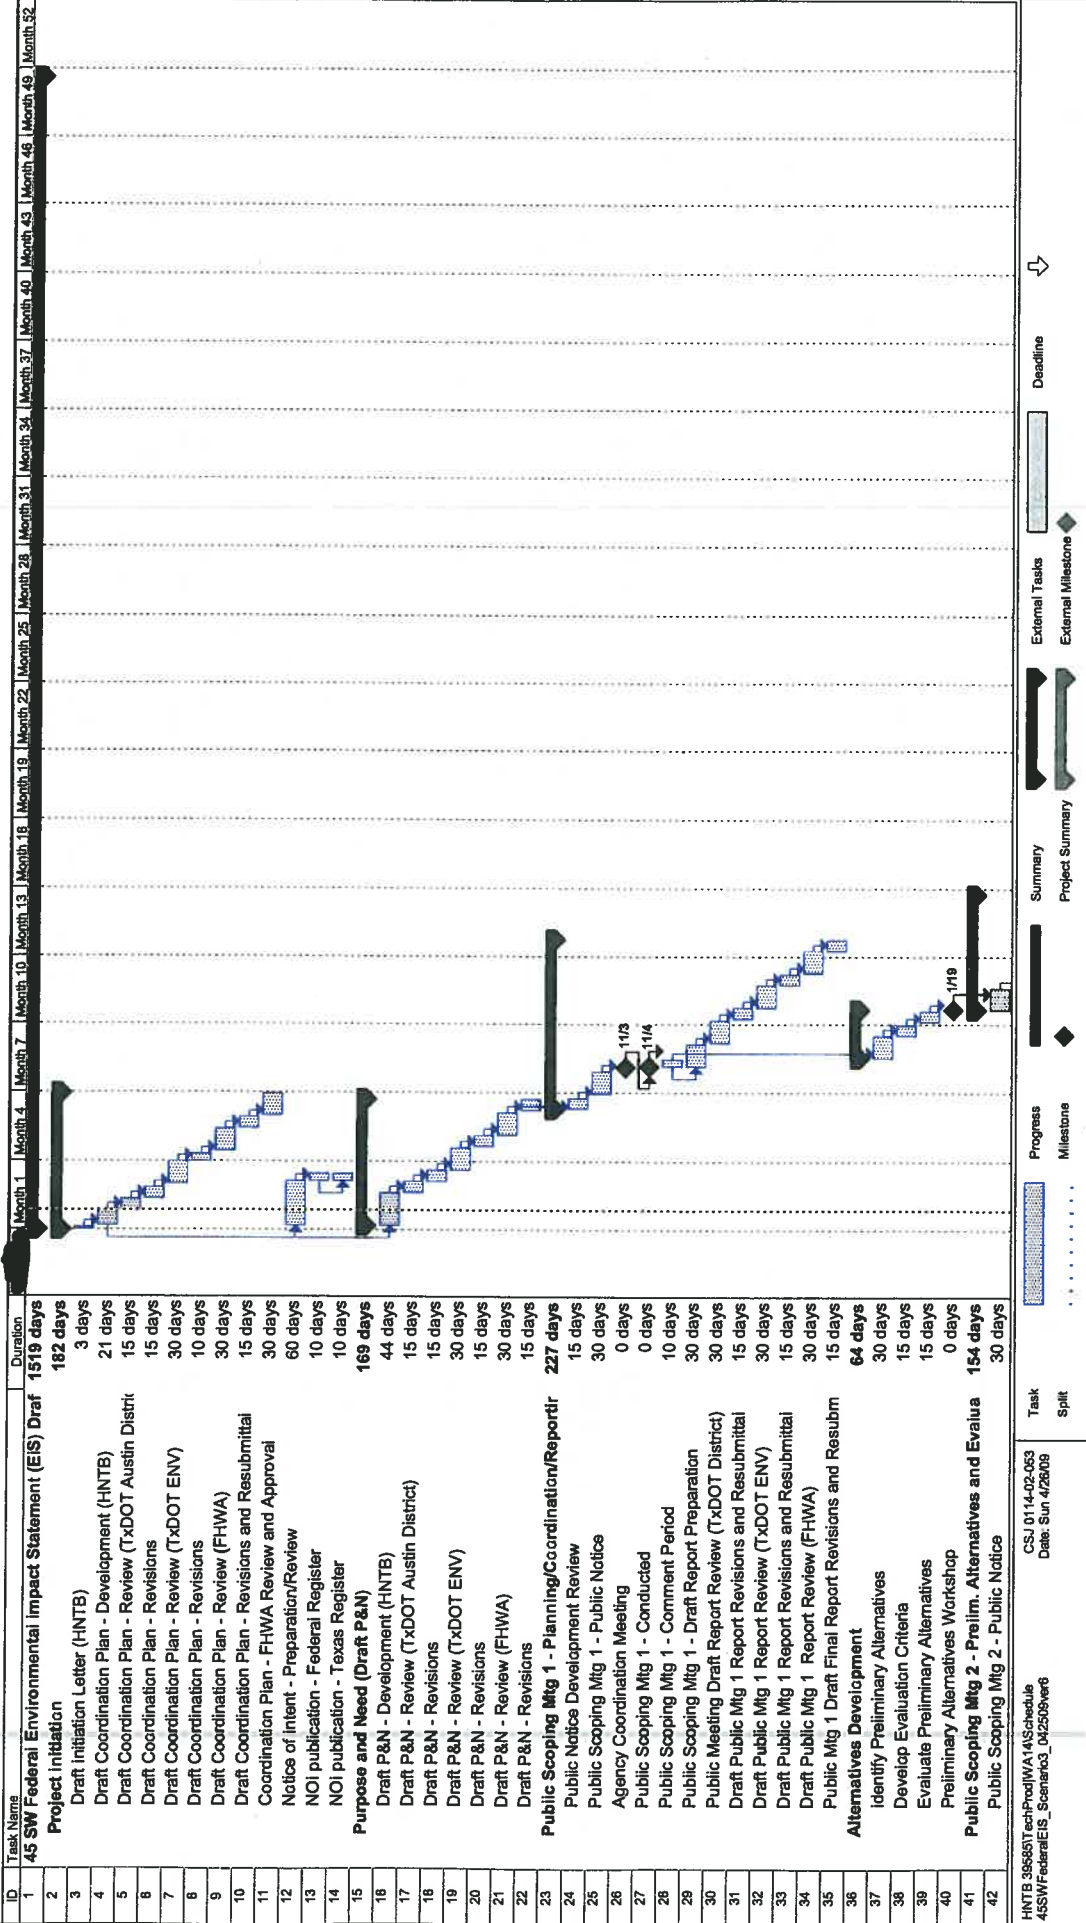


ID	Task Name	Duration
1	45 SW Federal Environmental Impact Statement (EIS) Draft	1519 days
2	Project Initiation	182 days
3	Draft Initiation Letter (HNTB)	3 days
4	Draft Coordination Plan - Development (HNTB)	21 days
5	Draft Coordination Plan - Review (TxDOT Austin District)	15 days
6	Draft Coordination Plan - Revisions	15 days
7	Draft Coordination Plan - Review (TxDOT ENV)	30 days
8	Draft Coordination Plan - Revisions	10 days
9	Draft Coordination Plan - Review (FHWA)	30 days
10	Draft Coordination Plan - Revisions and Resubmittal	15 days
11	Coordination Plan - FHWA Review and Approval	30 days
12	Notice of Intent - Preparation/Review	60 days
13	NOI publication - Federal Register	10 days
14	NOI publication - Texas Register	10 days
15	Purpose and Need (Draft P&N)	169 days
16	Draft P&N - Development (HNTB)	44 days
17	Draft P&N - Review (TxDOT Austin District)	15 days
18	Draft P&N - Revisions	15 days
19	Draft P&N - Review (TxDOT ENV)	30 days
20	Draft P&N - Revisions	15 days
21	Draft P&N - Review (FHWA)	30 days
22	Draft P&N - Revisions	15 days
23	Public Scoping Mtg 1 - Planning/Coordination/Report	227 days
24	Public Notice Development Review	15 days
25	Public Scoping Mtg 1 - Public Notice	30 days
26	Agency Coordination Meeting	0 days
27	Public Scoping Mtg 1 - Conducted	0 days
28	Public Scoping Mtg 1 - Comment Period	10 days
29	Public Scoping Mtg 1 - Draft Report Preparation	30 days
30	Public Meeting Draft Report Review (TxDOT District)	30 days
31	Draft Public Mtg 1 Report Revisions and Resubmittal	15 days
32	Draft Public Mtg 1 Report Review (TxDOT ENV)	30 days
33	Draft Public Mtg 1 Report Revisions and Resubmittal	15 days
34	Draft Public Mtg 1 Report Review (FHWA)	30 days
35	Public Mtg 1 Draft Final Report Revisions and Resubmittal	15 days
36	Alternatives Development	64 days
37	Identify Preliminary Alternatives	30 days
38	Develop Evaluation Criteria	15 days
39	Evaluate Preliminary Alternatives	15 days
40	Preliminary Alternatives Workshop	0 days
41	Public Scoping Mtg 2 - Prelim. Alternatives and Evalua	154 days
42	Public Scoping Mtg 2 - Public Notice	30 days

HNTB 395957\ep\Proj\HVA\MS\Schedule  
45SWFederalEIS\_Scenario3\_042509v06  
CSJ 0114-02-053  
Date: Sun 4/28/09

45 SW Environmental Impact Statement

CSJ 0114-02-053

(Federal Approval) Schedule  
51 Months

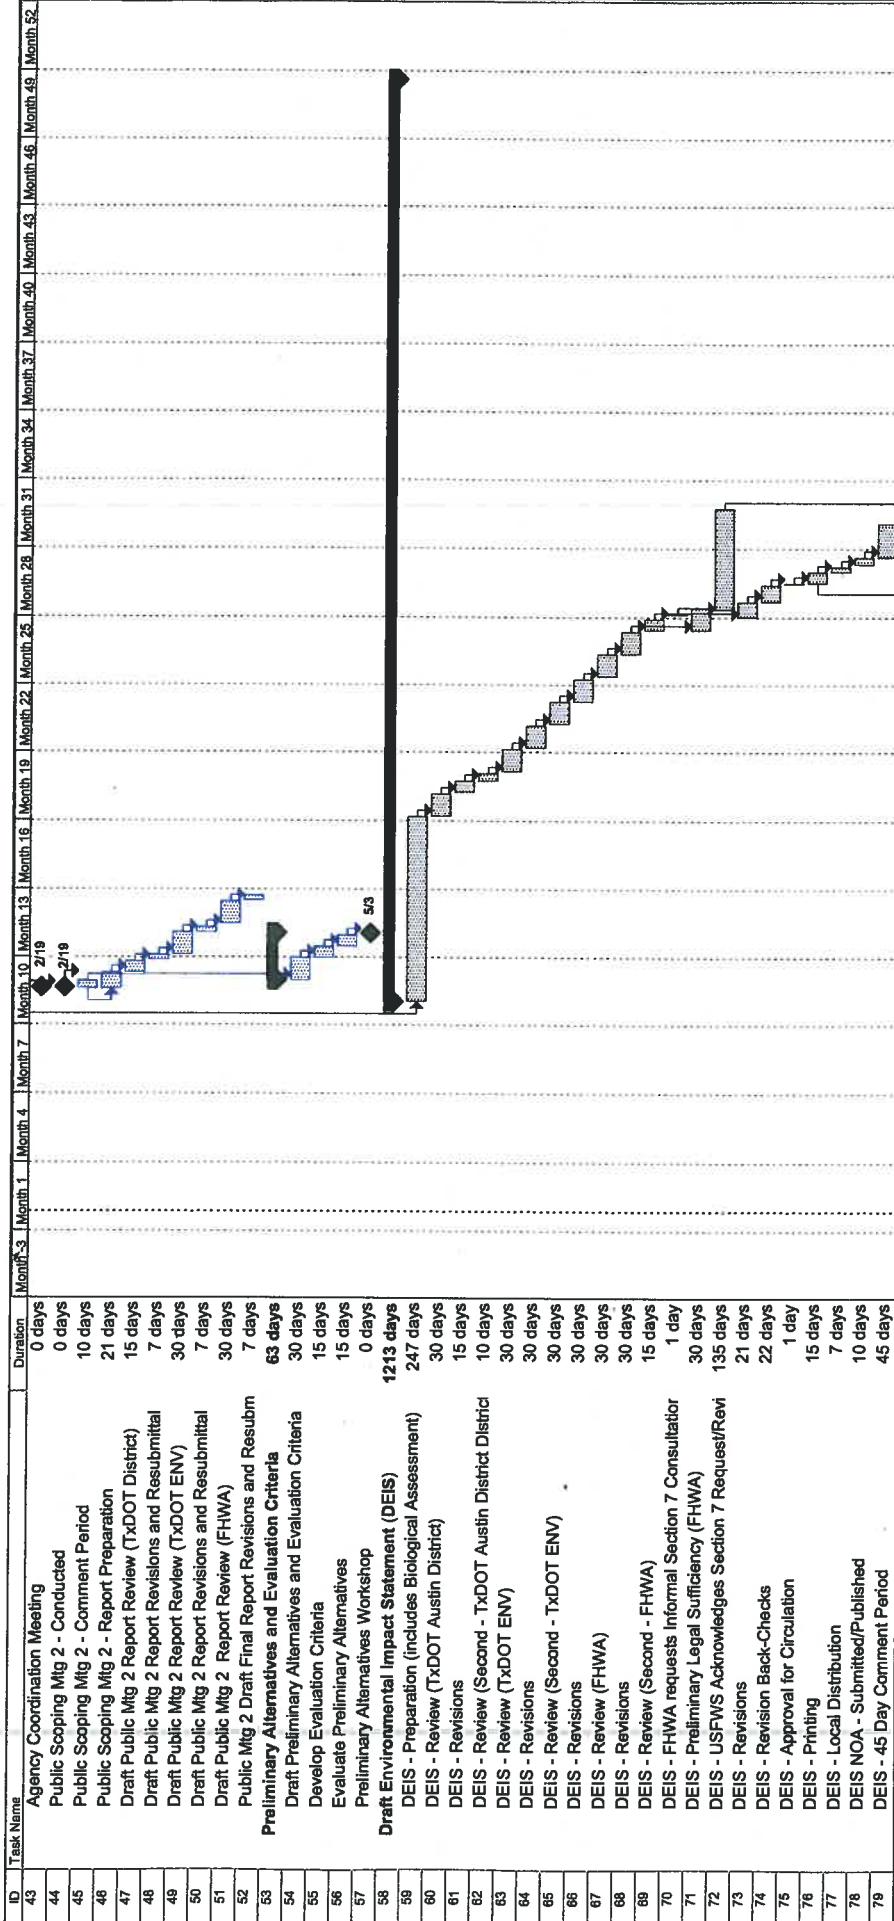

HNTB 395681T\_eap\Fed\IWA\14\Schedule  
45SWFederalEIS\_Scenario3\_042509ver6

CSJ 0114-02-053  
Date: Sun 4/25/09

Task Split

Progress Milestone

Summary Project Summary


External Tasks External Milestone

Deadline

45 SW Environmental Impact Statement

CSJ 0114-02-053

(Federal Approval) Schedule  
51 Months

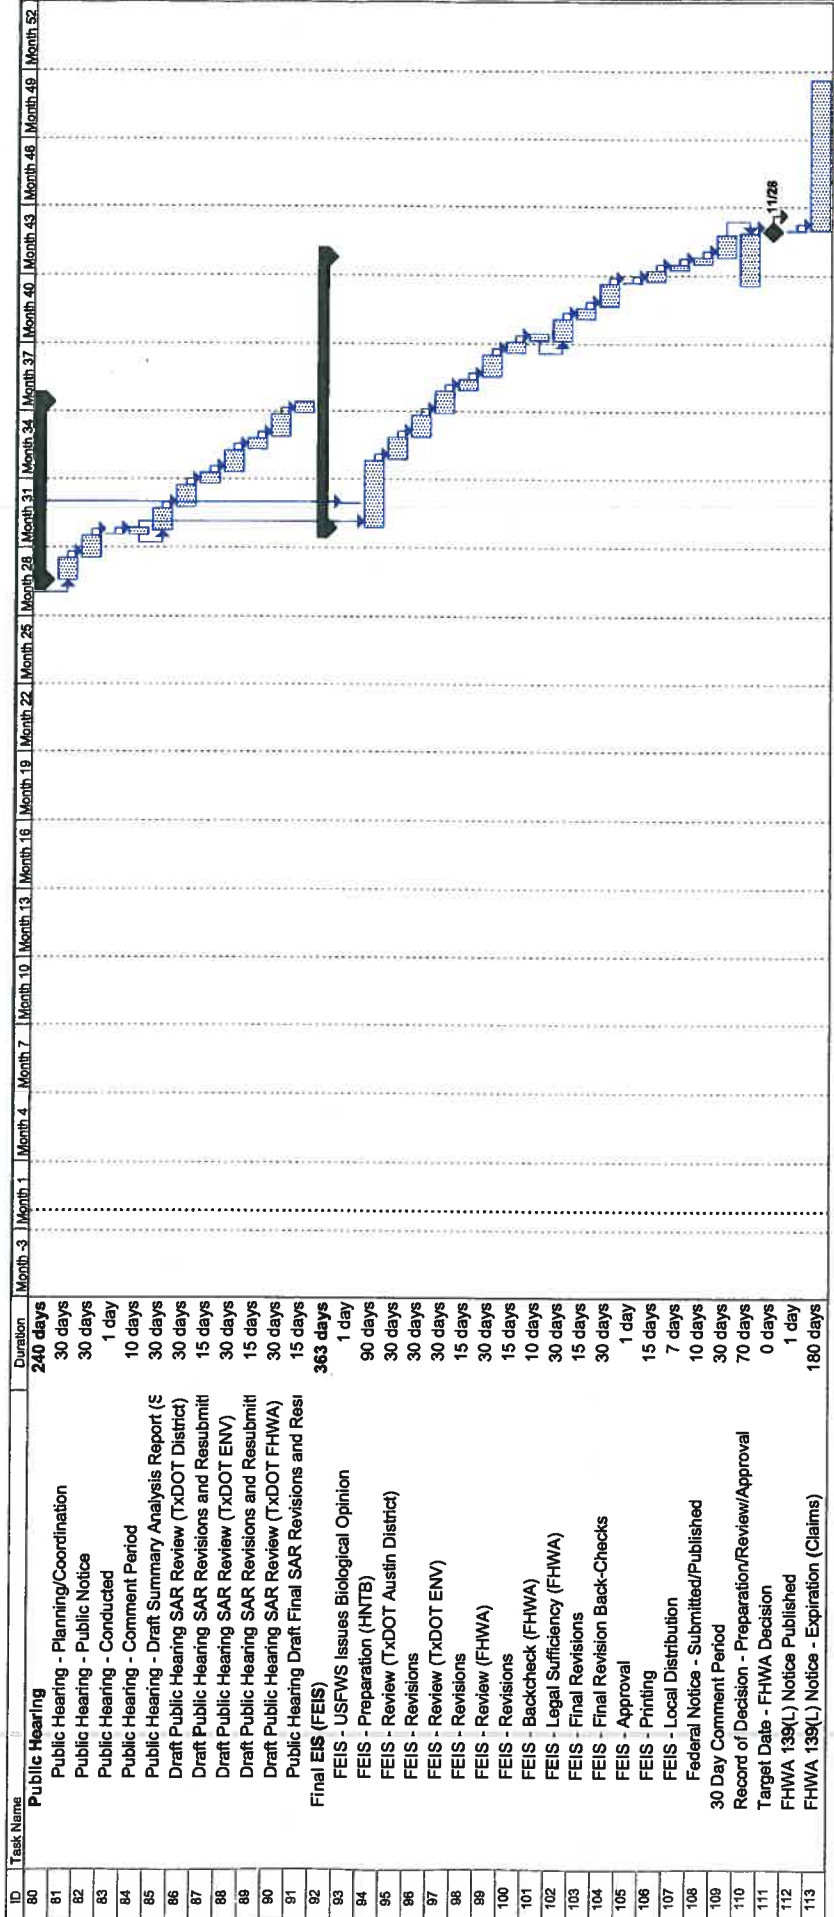

HNTB 39585T acnProc\WA\4\Schedule 45SW\FederalEIS\_Scenar03\_042509ver6 CSJ 0114-02-053 Date: Sun 4/26/09

Task Split

Progress Milestone

Summary Project Summary

External Tasks External Milestone

Deadline
